

GOVERNMENT OF GILOTT-BALTISTAN HEALTH DEPARTMENT GILOIT-BALTISTAN SECRETARIAT

No. Sec 11-6(104)/2024-25 Gilgit Date, 24th January, 2025

Th

The Procurement Committee.

Establishment of 50 bedded Cardiac Hospital,

Gilgit

Subject:

REQUEST FOR APPROVAL OF FINAL EVALUATION REPORT OF PROCUREMENT COMMITTEE 50 BEDDED CARDIAC HOSPITAL GILGIT FOR PROCUREMENT OF BIO MEDICAL EQUIPMENT

l am directed to forward herewith a copy of Director EPI health Department GB/ Chairman Procurement Committee 50 Bedded Cardiac Hospital Gilgit letter No.1711(2)/EPI/Estb/2023 dated 20th January, 2025 on the subject cited above and to say that the Secretary/PAO Health Department Gilgit-Baltistan has been pleased to approve the evaluation report for procurement of Bio-Medical equipments for the PSDP project titled "Establishment of 50 Bedded Cardiac Hospital at Gilgit".

Further action may be taken accordingly, please.

(GHUKAM MUHAMMAD) SECTION OFFICER (DEV.)

Cc.

The Project Director 50 Bedded Cardiac Hospital Gilgit.

The Medical Superintendent 50 Bedded Cardiac Hospital Gilgit.

3. The Drawing & Distribution Officer 50 Bedded Cardiac Hospital Gilgit.


PS to Secretary Health GB.

FINAL EVALUATION REPORT

Name of Procuring Agency ESTABLISHMENT OF 50 BEDDED CARDIAC HOSPITAL GILGIT DEPARTMENT OF HEALTH GOVERNMENT OF GILGIT-BALTISTAN

Title of Procurement

PROCUREMENT OF BIO-MEDICAL EQUIPMENT UNDER PSDP PROJECT "ESTABLISHMENT OF 50 BEDDED CARDIAC HOSPITAL, GILGIT"

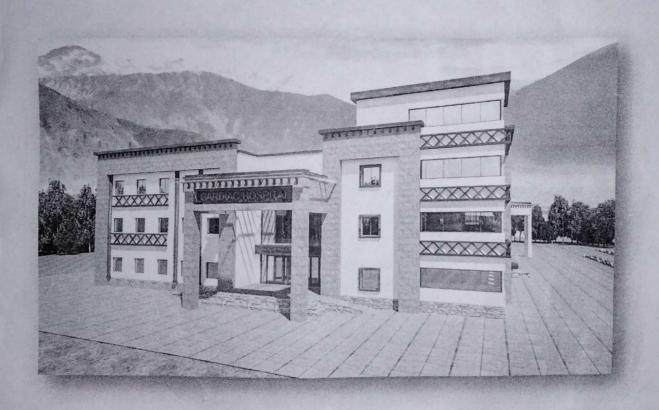

50 BEDDED CARDIAC HOSPITAL GILGIT

DEPARTMENT OF HEALTH

GOVERNMENT OF GILGIT-BALTISTAN



| | BACKGROUND: |
|-----|--|
| 1.1 | Department of Health, Gilgit Baltistan invited bids from the eligible suppliers for the procurement of biomedical equipment under the PSDP Project titled "Establishment of 50 bedded Cardiac Hospital, Gilgit." |

| | | | ECHNICAL EV BASIC D | |
|------|--------------------------------------|--------------------------|--|---|
| i) | Name of Procuring Agency: | | diameters. | nent of 50 Bedded Cardiac Hospital Gilgit Department of Health Government of Gilgit-Baltistan |
| ii) | P | Method of Procurement | Single Stage - Two Envelopes Procedure. | |
| iii) | Title | of Procurement | INVITATION TO BIDS FOR PROCUREMENT OF BIOMEDICAL EQUIPMENT | |
| iv) | Tene | der Publication: | Daily Newspa | apers, GB-PPRA & PPRA Website |
| | | | | TENDER PUBLICATION |
| | | Leading daily nev | | |
| | (a) | Tender Notice | PANALUA III | |
| | | in the Newspapers | | DAILY BUSINESS RECORDER (NATIONAL, ENGLISH) |
| | | Newspapers | DATED | 13 th September, 2024 |
| | | | 126 | DAILY DUNYA, ISLAMABAD (NATIONAL, URDU) |
| | | | DATED | 13 th September, 2024 |
| | | Elegrosur 1800 | | DAILY K-2 GB (LOCAL, URDU) |
| | | | DATED | 13 th September, 2024 |
| | | 15 YEAR (1990) -11 | | Daily Himalaya Today GB (LOCAL, URDU) |
| | | | DATED | 13th September, 2024 |
| | | | 2 | Daily Inhisar, GB |
| | | | DATED | 13th September, 2024 |
| | | The second | | Daily Bang e Sahar, GB |
| | | | DATED | 13 th September, 2024 |
| | (b) Advertisement on GB-PPRA website | | TO SEE SHIPE SEE | GB-PPRA TENDER NO. TSE-20240913215 |
| | | | | DATED OF PUBLICATION: 14 TH SEPTEMBER, 2024 |

| | (c) | Advertisement on PPRA website | ephetival ente | PPRA TENDER NO. TS-547679E | |
|-------|--|---|---|---|--|
| | | | The production | DATED OF PUBLICATION: 12 TH SEPTEMBER, 2024 | |
| v) | | and Time of Bid nission Closing | 101 | TH October, 2024 at 01:30 p.m. | |
| vi) | Date and Time of Technical Bid Opening | | 107 | TH October, 2024 at 02:00 p.m. | |
| vii) | Pre | e-Bid Meeting | The second second | 23-09-204 at 10:00 am | |
| viii) | T | nded Date and Time of Bid nission Closing | 29 | th October, 2024 at 01:30 p.m. | |
| ix) | Tim B | nded Date and e of Technical id Opening | <u>29</u> ^t | th October, 2024 at 02:00 p.m. | |
| x) | Ad | blication Of dendum for ension of Bid | B 363 (2, 12) | AILY BUSINESS RECORDER (NATIONAL, ENGLISH) | |
| | Su | bmission & | DATED | 09th October, 2024 | |
| | Opening | | DAILY DUNYA, ISLAMABAD (NATIONAL, URDU) | | |
| | | MEDISTRANCE. | DATED | 09th October, 2024 | |
| | | 80 S 31 V.M.A | | DAILY K-2 GB (LOCAL, URDU) | |
| | | alminer in | DATED | 09th October, 2024 | |
| | inatora Foday 68 | | Daily Himalaya Today GB (LOCAL, URDU) | | |
| | | | DATED | 09th October, 2024 | |
| | | | DATED | Daily Inhisar, GB | |
| xi) | Ad | ldendum on | DATED | 09 th October, 2024 | |
| , | THE RESERVE OF THE PARTY OF THE | PPRA website | | 09th October, 2024 | |
| xii) | Ad PF | Idendum on PRA website | | 09th October, 2024 | |
| | Total E | Bids Received again led in Technical Pro | st each packag | ge on Closing Date & Time and No. of Bids | |
| // | | A 200 | As C | | |

| Package No. | Package Name | No. of Bids Received | No. of Bids Qualified in Technical Evaluation |
|----------------|--|-------------------------|--|
| 1 | Anaesthesia machine with ventilator | 03 | 01 |
| 2 | Bipap & CPAP | 02 | 02 |
| 3 | Cerebral oximeter | 02 | 01 |
| 4 | Docking Station, infusion & syringe pump | 04 | 01 |
| 5 | ICU Ventilator | 04 | 01 |
| 6 | Neonatal Ventilator | 02 | 02 |
| 7 | ETT Machine | 04 | 02 |
| 8 | Holter Monitor | 02 | 01 |
| 9 | Telemetry System | 01 | 01 |
| 10 | Cardiac Monitor | 03 | 02 |
| 11 | Defibrillator | 03 | 01 |
| 12 | ECG Machine | 04 | 01 |
| 13 | Signal Average Machine | 02 | 01 |
| 14 | Tilt system | 02 | 01 |
| 15 - 19 | Scopes | 02 | 00 |
| 20 | Modular OT | 02 | 02 |
| 21 | Heart Lung Machine | 02 | 02 |
| 22 | IABP | 02 | 01 |
| 23 | Hypothermia | 04 | 01 |
| 24 | Blood warmer | 03 | 01 |
| 25 | Fabricator with alligators | Nil | 00 |
| 26-29 | OT Lights | 05 | 01 |
| 30 | Head Lights | Nil | 00 |
| 31 | Operation table | 03 | 00 |
| 32 | Gyne OT table | 01 | 00 |
| 33 | Vacuum extractor | Nil | 00 |
| 34 | Delivery table | 02 | 00 |
| 35 | Suction machine | 03 | 00 |
| 36 | Diathermy machine | 02 | 00 |
| 37 | Sternum saw | 02 | 01 |
| 38 | Sternum saw RS | 02 | 01 |
| 39 | ACT Machine | 02 | 01 |
| 40 | Gama camera | 01 | 01 |
| 41 | Echo | 02 | 01 |
| 42 | Ultrasound machine | 02 | 00 |
| 43 | Temporary pacemaker | 01 | 01 |
| 44 | Blood gas analyser | 04 | 00 |
| 45 | Elisa system | 02 | 00 |
| 46 | ESR machine | 01 | 00 |

| | 0.110 | 01 | 00 |
|--|--|--|--|
| 47 | | 03 | 00 |
| 48 Chemistry analyser 49 Coagulation Meter | | 02 | |
| | | 02 | 00 |
| 50 | | 03 | 00 |
| 51 | 0.7 | 03 | 00 |
| 52 | | 02 | 01 |
| 53 | | 02 | 00 |
| 54 | CSSD | | 02 |
| 55 | | 04 | 01 |
| 56 | Medical gasses | 04 | 01 |
| 57 | The state of the s | Nil | 00 |
| 58 | Dental treatment unit | 04 | 01 |
| 59 | Complete set of surgical instruments | 04 | 00 |
| 60 | Gynae Instrument Complete | 05 | 01 |
| | The state of the s | | |
| 03 | PREPERATION OF THE BIDDING DOCUMENTS: | The same of the sa | |
| 3.2 | 23n dated 12th February, 2024 (attached vide An house Islamabad from 24th to 27th May 2024, min Annex - B . The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter no dated 28th August, 2024 issued directives to amend | utes of meeting lealth Secretaria o. Sec-H-6(104) | attached v |
| 3.2 | house Islamabad from 24th to 27th May 2024, min Annex - B . The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C . In order to comply with the directives of Health procurement committee was convened from 31st Annex - C. | lealth Secretaria b. Sec-H-6(104), I the draft biddi the Secretariat, m | at for approved the street of |
| | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st At 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. | lealth Secretaria b. Sec-H-6(104), I the draft biddi the Secretariat, m | at for approved the street of |
| | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st At 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. APPROVAL OF THE BIDDING DOCUMENTS: | lealth Secretaria b. Sec-H-6(104), I the draft biddi th Secretariat, magust, 2024 to 0 document. Minu | at for approved the second sec |
| 3.3 | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st Ac 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. APPROVAL OF THE BIDDING DOCUMENTS: Draft Bidding documents incorporating the directives. | lealth Secretaria b. Sec-H-6(104), I the draft biddi th Secretariat, managust, 2024 to 0 document. Minu | at for approved the second sec |
| 3.3 | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st Ac 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. APPROVAL OF THE BIDDING DOCUMENTS: Draft Bidding documents incorporating the directive submitted to Health Secretariat GB for approval and the secreta | lealth Secretaria b. Sec-H-6(104), I the draft biddi th Secretariat, magust, 2024 to 0 document. Minu | at for approved has a stacked visual for approximation for app |
| 3.3 | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st At 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. APPROVAL OF THE BIDDING DOCUMENTS: Draft Bidding documents incorporating the directive submitted to Health Secretariat GB for approval at the PAO/Secretary Health GB vide Health Secretariat GB vide Vide Health Secretariat GB vide Vide Vide Vide Vide | lealth Secretaria b. Sec-H-6(104), I the draft biddi th Secretariat, magust, 2024 to 0 document. Minutes wes of Health Secretariat has | at for approved by a start at were approximately approxima |
| 3.3 | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st Az 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. APPROVAL OF THE BIDDING DOCUMENTS: Draft Bidding documents incorporating the directive submitted to Health Secretariat GB for approval are the PAO/Secretary Health GB vide Health Sec 6(104)/2024-25 dated 6th September, 2024. Letter | lealth Secretaria b. Sec-H-6(104), I the draft biddi th Secretariat, magust, 2024 to 0 document. Minutes wes of Health Secretariat has | at for approved by a start at were approximately approxima |
| 3.3 04 | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st Ac 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. APPROVAL OF THE BIDDING DOCUMENTS: Draft Bidding documents incorporating the directive submitted to Health Secretariat GB for approval and the PAO/Secretary Health GB vide Health Sec 6(104)/2024-25 dated 6th September, 2024. Letter PRE-BID MEETING: | lealth Secretaria o. Sec-H-6(104), d the draft biddi on Secretariat, in ugust, 2024 to 0 document. Minu oves of Health Secretariat letter attached vide A | at for approved the second section of the section o |
| 3.3 04 | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st Ac 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. APPROVAL OF THE BIDDING DOCUMENTS: Draft Bidding documents incorporating the directive submitted to Health Secretariat GB for approval and the PAO/Secretary Health GB vide Health Sec 6(104)/2024-25 dated 6th September, 2024. Letter PRE-BID MEETING: As per the advertisement & approved bidding documents. | lealth Secretaria o. Sec-H-6(104), d the draft biddi h Secretariat, magust, 2024 to 0 document. Minu less of Health Secretariat letter attached vide A | at for approved to the standard of the standar |
| 3.3 04 | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st At 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. APPROVAL OF THE BIDDING DOCUMENTS: Draft Bidding documents incorporating the directive submitted to Health Secretariat GB for approval and the PAO/Secretary Health GB vide Health Sec 6(104)/2024-25 dated 6th September, 2024. Letter PRE-BID MEETING: As per the advertisement & approved bidding documented on 23-09-204 at 10:00 am at the conference is | lealth Secretaria o. Sec-H-6(104), d the draft biddi h Secretariat, magust, 2024 to 0 document. Minu less of Health Secretariat letter attached vide A | at for approved to the standard of the standar |
| 3.3 04 05 | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st At 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. APPROVAL OF THE BIDDING DOCUMENTS: Draft Bidding documents incorporating the directive submitted to Health Secretariat GB for approval and the PAO/Secretary Health GB vide Health Sec 6(104)/2024-25 dated 6th September, 2024. Letter PRE-BID MEETING: As per the advertisement & approved bidding documented on 23-09-204 at 10:00 am at the conference Feminutes of meeting attached vide Annex - F | lealth Secretarias b. Sec-H-6(104), d the draft biddi h Secretariat, magust, 2024 to 0 document. Minus ves of Health Secretariat letter attached vide A ment, the Pre-Bid Hall of Gilgit Care | at for approved to the standard of the standar |
| 3.3 04 05 | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st At 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. APPROVAL OF THE BIDDING DOCUMENTS: Draft Bidding documents incorporating the directive submitted to Health Secretariat GB for approval and the PAO/Secretary Health GB vide Health Sec 6(104)/2024-25 dated 6th September, 2024. Letter PRE-BID MEETING: As per the advertisement & approved bidding documents of meeting attached vide Annex - F EXTENSION IN BID SUBMISSION & CLOSING DAT Initially 10 TH October, 2024 at 01:30 p.m. was set as the second process. | lealth Secretaria o. Sec-H-6(104), d the draft biddi h. Secretariat, magust, 2024 to 0 document. Minutes of Health Secretariat letter attached vide Ament, the Pre-Bid Hall of Gilgit Care | at for approved the second of |
| 3.3 04 05 | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st Az 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. APPROVAL OF THE BIDDING DOCUMENTS: Draft Bidding documents incorporating the directive submitted to Health Secretariat GB for approval at the PAO/Secretary Health GB vide Health Sec 6(104)/2024-25 dated 6th September, 2024. Letter PRE-BID MEETING: As per the advertisement & approved bidding documented on 23-09-204 at 10:00 am at the conference of Minutes of meeting attached vide Annex - F EXTENSION IN BID SUBMISSION & CLOSING DAT Initially 10TH October, 2024 at 01:30 p.m. was set as to bids. During the pre-bid meeting majority of the | lealth Secretaria b. Sec-H-6(104), I the draft biddi ch Secretariat, magust, 2024 to 0 document. Minus ves of Health Secretariat letter attached vide A ment, the Pre-Bid Hall of Gilgit Care the last date for secretariat date for secretariat date. | at for approved by the submission of the submiss |
| 3.3 04 05 | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st At 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. APPROVAL OF THE BIDDING DOCUMENTS: Draft Bidding documents incorporating the directive submitted to Health Secretariat GB for approval at the PAO/Secretary Health GB vide Health Sec 6(104)/2024-25 dated 6th September, 2024. Letter PRE-BID MEETING: As per the advertisement & approved bidding documented on 23-09-204 at 10:00 am at the conference of Minutes of meeting attached vide Annex - F EXTENSION IN BID SUBMISSION & CLOSING DAT Initially 10TH October, 2024 at 01:30 p.m. was set as to bids. During the pre-bid meeting majority of the extension of bid submission date therefore the local content of the submission date therefore the local content of | lealth Secretaria b. Sec-H-6(104), If the draft biddi ch Secretariat, magust, 2024 to 0 document. Minus ves of Health Secretariat letter attached vide A ment, the Pre-Bid Hall of Gilgit Card E bidders reque | at for approved the same of th |
| 3.3 04 05 | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st Ac 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. APPROVAL OF THE BIDDING DOCUMENTS: Draft Bidding documents incorporating the directive submitted to Health Secretariat GB for approval and the PAO/Secretary Health GB vide Health Sec 6(104)/2024-25 dated 6th September, 2024. Letter PRE-BID MEETING: As per the advertisement & approved bidding documents of meeting attached vide Annex - F EXTENSION IN BID SUBMISSION & CLOSING DAT Initially 10 TH October, 2024 at 01:30 p.m. was set as to bids. During the pre-bid meeting majority of the extension of bid submission date therefore the lass were extended to 29th October, 2024 at 01:30 p.m. and | lealth Secretaria b. Sec-H-6(104), If the draft biddi ch Secretariat, magust, 2024 to 0 document. Minus ves of Health Secretariat letter attached vide A ment, the Pre-Bid Hall of Gilgit Card E bidders reque | at for approved the same of th |
| 3.3 04 05 | house Islamabad from 24th to 27th May 2024, min Annex - B. The draft bidding documents were submitted to Hand in response Health Secretariat GB vide letter not dated 28th August, 2024 issued directives to amend Letter attached vide Annex - C. In order to comply with the directives of Health procurement committee was convened from 31st Az 2024 at GB House Islamabad to finalize the bidding attached vide Annex - D. APPROVAL OF THE BIDDING DOCUMENTS: Draft Bidding documents incorporating the directive submitted to Health Secretariat GB for approval at the PAO/Secretary Health GB vide Health Sec 6(104)/2024-25 dated 6th September, 2024. Letter PRE-BID MEETING: As per the advertisement & approved bidding documented on 23-09-204 at 10:00 am at the conference of Minutes of meeting attached vide Annex - F EXTENSION IN BID SUBMISSION & CLOSING DAT Initially 10TH October, 2024 at 01:30 p.m. was set as to bids. During the pre-bid meeting majority of the | lealth Secretaria b. Sec-H-6(104), If the draft biddi ch Secretariat, magust, 2024 to 0 document. Minus ves of Health Secretariat letter attached vide A ment, the Pre-Bid Hall of Gilgit Card E bidders reque | at for approved the same of th |

| 07 | MEETING OF GREVIANCE REDRESSAL COMMITTEE: |
|--|--|
| 7.1 | In order to address the grievances of bidders on the bidding documents the |
| adjord i | meeting of GRC notified by the Health Secretariat vide Notification No. Sec. II. |
| arb gar | 6(104)/2023-24 dated 20th January, 2024 (attached vide Annex - C) was |
| | convened on 15th October, 2024 at EPI Conference Hall. |
| 7.2 | Recommendations/Decisions of the GRC were made part of the Bidding |
| | Documents and minutes were issued to all bidders. Minutes of the GRC attached |
| | vide Annex - H. |
| 08 | OPENING OF PROPOSALS: |
| | In order to open the bids meeting of the Procurement Committee was convened |
| | on 29th October 2024 at 1:30PM in the conference hall of Gilgit Cardiac Hospital |
| | Minutes of the meeting attached vide Annex - I |
| 09 | MEETING OF THE PROCUREMENT COMMITTEE FOR EVALUATION OF THE |
| | TECHNICAL PROPOSAL: |
| 9.1 | In order to evaluate the technical proposal meeting of the procurement |
| | committee was convened from 10th December, 2024 to 17th December, 2024 at |
| | Conference Hall of Cardiac Hospital Gilgit. |
| 9.2 | Following members of the procurement committee attended the meeting: |
| | Attendance Sheet attached vide Annex - J. |
| THE RESERVE OF THE PARTY OF THE | |

| SR. NO. Name | | Designation | |
|-----------------|-------------------------------------|--|--|
| 1 | Dr Syed Sadiq Shah Director, EPI-GB | | |
| 2 | Engr. Shahid Masood | PD, 50 bedded Cardiac Hospital Gilgit | |
| 3 | Syed Ishtiaq Hussain | Director, SHPI-GB | |
| 4 | Dr. Faheem Iqbal | Consultant Cardiologist, 50 bedded Cardiac Hospital Gilgit | |
| 5 | Aziz Haider | DD(P), DHS Baltistan | |
| 6 | Engr. Shabbir Hussain | BME, DHS(P) Gilgit | |
| 7 | Muhammad Ali | Finance Officer, FD-GB | |
| 8 | Muhammad Harith | RO, P&D D GB | |
| 9 | Engr. Umair Kabeer | BME, PIC Lahore | |
| 10 | Engr. Mohsin Ali | BME, Shifa Int Hosp Islamabad | |
| 11 | Engr. Rizwan | BME, RIC Rawalpindi | |

Engr. Irshad Wali, also attended the proceedings and facilitated the Technical Evaluation as representative of the Consultant PEPAC in compliance with the Health Secretariat Letter No. Sec-H-6(104)/2024-25 dated 16th September, 2024. Letter Attached vide **Annex - K**.

| | 1 o(101)/2021 25 dated 10 September, 2021. Better Attached vide Aimex - K. |
|------|--|
| 10 | PROCEEDINGS OF TECHNICAL EVALUATION: |
| 10.1 | Package wise evaluation of the technical proposals was carried out by the |
| | Procurement committee. |
| 10.2 | Procurement committee thoroughly examined the technical proposals in accordance with the Technical Evaluation criteria mentioned in the Bidding Documents. |
| | |

11 VERIFICATIONS OF DOCUMENTARY EVIDENCE INCLUDING CDR:

Mysail

A W

A SA

m An

The Procurement committee decided that the documentary evidences including CDRs provided by the bidder, may be verified if deemed necessary at any stage of the procurement process. If any of the documentary evidences provided by the bidders is found fake the bidder will be disqualified at any stage during the procurement process. TECHICAL EVALUATION RESULTS: Package wise Technical Evaluation Report is Attached (Annex - K) 12

| .1 In order to address the Grievances Report meeting of the GRC was con .2 Minutes of GRC is attached (Annex | |
|--|---------|
| Pe. | 2 MgSw/ |
| | |
| 24/ | |
| | |
| | |

| 14 | FINANCIAL PROPOSAL OPENING |
|------|---|
| 14.1 | Meeting of the procurement committee, constituted for the procurement of biomedical equipment for the PSDP project titled "Establishment of 50 Bedded Cardiac Hospital Gilgit", was called on by The Chairman of Procurement Committee 50 bedded Cardiac vide letter dated 08th January, 2025 |
| 14.2 | Following members of the procurement committee attended the meeting. (attendance sheet attached). |

| Sr. No. | Name of Member | Department | Designation | Membership | |
|---------|-----------------------|---|----------------------------|------------|--|
| 1 | Dr Syed Sadiq Shah | EPI-Gilgit Baltistan | Director | Chairman | |
| 2 | Engr. Shahid Masood | 50 bedded Cardiac Hospital, Gilgit. | Project Director | Member | |
| 3 | Syed Ishtiaq Hussain | SHPI- Gilgit Baltistan | Director | Member | |
| 4 | Dr. Faheem Iqbal | Gilgit Cardiac Hospital | Consultant Cardiologist | Member | |
| 5 | Aziz Haider | DD(P) | DHS Baltistan | Member | |
| 6 | Engr. Shabbir Hussain | DHS(P) Gilgit | Bio Medical Engineer | Member | |
| 7 | Muhammad Ali | FD- Gilgit Baltistan | Finance Officer | Member | |
| 8 | Muhammad Harith | P&D D GB | RO | Member | |
| 9 | Engr. Umair Kabeer | Punjab Institute of Cardiology, Lahore. | Bio Medical Engineer | Member | |
| 10 | Engr. Mohsin Ali | Shifa International Hospital Islamabad. | Bio Medical Engineer | Member | |
| 11 | Engr. Rizwan | Rawalpindi Institute of Cardiology, Rawalpindi. | Bio Medical Engineer | Member | |

Following representatives of the Bidders/Firms also attended the meeting; (attendance sheet attached)

| | Sr. No. | Name of Representative | Firm |
|----|------------|------------------------|----------------------------------|
| | 1 | Mr. Khalid | M/s Radiant Medical Pvt. Ltd. |
| .3 | 2 | Mr. M. Mehboob Saqib | M/s Mediland Pakistan Pvt. Ltd. |
| | 3 | Mr. M. Ishfaq | M/s Medequips (SMC) Pvt. Ltd. |
| | 4 | Mr. Irfan Akram | M/s Vertex Medical Pvt. Ltd. |
| | 5 | Mr. Farooq Ahmed | M/s Jamil Enterprises |
| | 6 | Mr. Zain Ajmal | M/s Shirazi Trading Pvt. Ltd. |
| | 7 | Mr. Muhammad Imran | M/s Total Technologies Pvt. Ltd. |

Meeting started with the recitation of Holy Quran; the chair formally welcomed all members of the committee.


The Procurement Committee opened the sealed financial proposals of the responsive bidders of the Technical Proposal Evaluation.

Lot wise sealed Financial Proposals were opened and the prices quoted were read aloud and noted.

14.7 Following is the lot wise comparative statement of rates offered by the bidders;

mani .









| em / acka e No. | Item Name | Estimated Cost | Name Of Company | Price / Rate | Remarks |
|-----------------------|---|--------------------|---------------------------------|-----------------|--------------------|
| A REEL | | CA MANAGEMENT | Shirazi Trading | 51,500,000 | 1st Lowes |
| 1 | Anaesthesia Machine with Ventilator | 28,500,000 | Noor International | N/A | Non- Responsiv |
| | | THE REAL PROPERTY. | Total Technologies | N/A | Non- Responsiv |
| 2 | BI-PAP & CPAP | 7,000,000 | Total Technologies | 3,785,000 | 1st Lowes |
| - | | anting . | Jamil Enterprise | 6,682,500 | 2nd Lowes |
| 3 | Cerebral Oximeter | 1,600,000 | Radiant Medical (Pvt)Ltd. | 7,788,000 | 1st Lowest |
| | Electric Control of the Park | 2,000,000 | Hospicare Systems | N/A | Non- Responsive |
| | Syringe Pump and Infusion Pump Docking Station | 17,500,000 | Medifa Enterprises | N/A | Non- Responsive |
| 4 | | | Irfan Brothers International | N/A | Non- Responsive |
| | | | Total Technologies | N/A | Non- Responsive |
| | | | Jamil Enterprise | 26,718,500 | 1st Lowest |
| | | 58,500,000 | Sahab International | N/A | Non- Responsive |
| 5 | ICU Ventilator | | Noor International | N/A | Non- Responsive |
| • | | | Chinar International | N/A | Non- Responsive |
| | | | Total Technologies | 71,457,048 | 1st Lowest |
| 6 | Noonatal Vantilatan | 8,000,000 | Mediland Pakistan | 42,281,284 | 1st Lowest |
| | Neonatal Ventilator | 8,000,000 | Total Technologies | N/A | Non- Responsive |
| | 14 | | Jamil Enterprise | N/A | Non- Responsive |
| 7 | ETT Machine | 11,000,000 | Hospicare Systems | N/A | Non- Responsive |
| 14 | A E monthous 1 estal | shell first To | Shirazi Trading | 19,830,000 | 2nd Lowest |
| | | Section 1 | Radiant Medical (Pvt) Ltd. | 16,422,236 | 1st Lowest |
| 8 | Holter Monitoring System | 4,500,000 | Hospicare Systems | N/A | Non- Responsive |
| 1.A | | | Jamil Enterprise | 11,500,000 | 1st Lowest |

| | | | -iaa | 14,000,000 | 1st Lowest |
|--------|---|--|---------------------------------|--|-------------|
| 9 | Telemetry System | 5,000,000 | Jamil Enterprise Medequips (SMC | 140,297,280 | 1st Lowest |
| | | | Pvt) Ltd. | 233,522,000 | 2nd Lowest |
| 10 | Monitors | 67,800,000 | Shirazi Trading | | Non- |
| | Monitors | 07,000, | Irfan Brothers | N/A | Responsive |
| | | | International | | Non- |
| | | | Shirazi Trading | N/A | Responsive |
| LI KIS | Mail 2000 CENTE 1192 | | | | Non- |
| 11 | Defibrillator | 33,000,000 | Radiant Medical (Pvt) Ltd. | N/A | Responsive |
| | | | Jamil Enterprise | 95,556,500 | 1st Lowest |
| | | 93,24 | | | Non- |
| | | | Jamil Enterprise | N/A | Responsive |
| | | | Hospicare | NI / A | Non- |
| | | 11,100,000 | Systems | N/A | Responsive |
| 12 | ECG Machine | 11,100,000 | Sahab | N/A | Non- |
| | International | International | N/A | Responsive | |
| | | ARLAND | Radiant Medical | 17,701,180 | 1st Lowest |
| | | | (Pvt) Ltd. | 17,701,100 | |
| | | | Radiant Medical | N/A | Non- |
| 13 | Signal Average ECG system | 2,100,000 | (Pvt)Ltd. | | Responsive |
| 2000 | | | Jamil Enterprise | 9,800,000 | 1st Lowest |
| ST. IN | Head up Tilt (HUTT) | | Mediland | N/A | Non- |
| 14 | System | 9,500,000 | Pakistan | | Responsive |
| | | | Jamil Enterprise | 45,500,000 | 1st Lowest |
| | Marie Andreis Park | | Allmed Solutions | N/A | Non- |
| 15-19 | Scopes | 17,790,000 | Medifa | | Responsive |
| | | | Enterprises | N/A | Non- |
| | | Market Ship | Total | | Responsive |
| | M. I. I. O The same | 104,000,00 | Technologies | 343,012,990 | 1st Lowest |
| 20 | Modular Operation Theatre | 0 | Radiant Medical | | |
| | Heart Lung Machine | 34,000,000 | (Pvt) Ltd. 405,313,008 | 405,313,008 | 2nd Lowest |
| | | | Mediland | | |
| 21 | | | Pakistan | | 1st Lowest |
| | | Description of | Vertex Pakistan | 257,482,470 | 2nd Lawrent |
| | THE REPORT OF THE PARTY OF THE | 48,000,000 | Shirazi Trading | | 2nd Lowest |
| 22 | IABP | 10,000,000 | | N/A | Non- |
| | | ON THE OWNER OF THE | Mediland | | Responsive |
| | | | Pakistan | N/A | Non- |
| | | 11,000,000 | Hospicare | N. C. | Responsive |
| | | | Systems | N/A | Non- |
| 23 | Hypothermia Machine | A CONTRACTOR OF THE PARTY OF TH | Jamil Enterprise | 59,600,000 | Responsive |
| | | | Mediland | | 1st Lowest |
| | | | Pakistan | N/A | Non- |
| | | | Vertex Pakistan | 6,291,376 | Responsive |
| 24 | Blood warmer | 3,600,000 | Radiant Medical | | 2nd Lowest |
| | - 20 | | (Pvt) Ltd. | 11,012,940 | 1st Lowest |
| my | A TO B | da | A CO | er plant | 11 |
| | | | | THE RESERVE OF THE PARTY OF THE | |

| ispure ! | 1 300.00EEEE] mile | C Results | Hospicare Systems | N/A | Non- Responsive |
|---------------------------------------|---|--|---------------------------------|------------|--------------------|
| | And Control | All whole | Irfan Brothers International | N/A | Non- Responsive |
| 25 | Fabricator with alligator clamp | Secretary of the secret | No Bid received | N/A | N/A |
| artent. | AM a conve | E fanyola I | Total Technologies | 27,287,941 | 2nd Lowest |
| | 3000 | | Jamil Enterprise | 26,011,250 | 1st Lowest |
| 26-29 | OT lights | 10,000,000 | Irfan Brothers International | N/A | Non- Responsive |
| | AN TON | Beet lot | Sahab International | N/A | Non- Responsive |
| BAISSCA | Operation Head light | mai limi | GMED | N/A | Non- Responsive |
| 30 | Operation Head light | | No Bid received | N/A | N/A |
| | AND | | GMED | N/A | Non- Responsive |
| 31 | Operation Table | 12,000,000 | Irfan Brothers International | N/A | Non- Responsive |
| Hydra va Santa | Marie Marie | | Sahab International | N/A | Non- Responsive |
| 32 | Gyne OT Table | 4,000,000 | GMED | N/A | Non- Responsive |
| 33 | Vacuum Extractor | Okmistati, L | No Bid received | N/A | N/A |
| 34 | Delivery Table | 2,500,000 | Irfan Brothers International | N/A | Non- Responsive |
| | | | GMED | N/A | Non- Responsive |
| | Suction Machine | 16,200,000 | Sahab International | N/A | Non- Responsive |
| 35 | | | Irfan Brothers International | N/A | Non- Responsive |
| 400 | EN PERMIT | Sanst | Medifa Enterprises | N/A | Non- Responsive |
| 36 | Diathermy Machine | 4,200,000 | GMED | N/A | Non- Responsive |
| | | | Irfan Brothers International | N/A | Non- Responsive |
| 37 | Sternum Saw | 5,070,000 | GMED | N/A | Non- Responsive |
| 20-17-03 | 100 A | | Jamil Enterprise | 21,570,000 | 1st Lowest |
| 38 | Sternum Saw (RS) | 3,600,000 | GMED | N/A | Non- Responsive |
| 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 | | Partie High Control | Jamil Enterprise | 7,600,000 | 1st Lowest |
| | | arts to the second | Jamil Enterprise | 6,340,000 | 1st Lowest |
| 39 | ACT Machine | 1,200,000 | Sahab International | N/A | Non- Responsive |

| 40 | Gamma Camera | 150,000,00 | Shirazi Trading | 313,500,000 | 1st Lowe |
|----|--|--------------------|---------------------------------|-----------------|------------------|
| | | 0 | Hoora Pharma | N/A | Non- Responsi |
| 41 | Echo Machines | 88,000,000 | Medequips (SMC Pvt) Ltd. | 157,680,000 | 1st Lowe |
| | | | BioTech Services | N/A | Non- Responsi |
| 42 | Ultrasound Machines | 19,500,000 | Medequips (SMC | N/A | Non- |
| 43 | Pacemakers | 0.100.000 | Pvt) Ltd. | 22,870,000 | Responsi |
| | | 8,100,000 | Jamil Enterprise Irfan Brothers | | Non- |
| | | | International | N/A | Respons |
| | | | mternational | | Non- |
| 44 | Blood Cas Aust | | Jamil Enterprise | N/A | Respons |
| | Blood Gas Analyzer | 2,500,000 | | Carlo Chicago | Non- |
| | | | Hoora Pharma | N/A | Respons |
| | | No. | Sahab | | Non- |
| | | | International | N/A | Respons |
| | | | Sahab | | Non- |
| 45 | Elisa System | 6,000,000 | International | N/A | Respons |
| | | 6,000,000 | Irfan Brothers | NI /A | Non- |
| | | | International | N/A | Respons |
| 46 | ESR Machine | 1,600,000 | Sahab | N/A | Non- |
| | | 2,000,000 | International | IV/A | Respons |
| 47 | Cell Separator | 8,300,000 | Hoora Pharma | N/A | Non- |
| | | | | 11/11 | Respons |
| | | THE REAL PROPERTY. | Hoora Pharma | N/A | Non- |
| 40 | | 9,500,000 | Irfan Brothers | / | Respons |
| 48 | Chemistry Analyzer | | International | N/A | Non- |
| | | | Sahab | | Respons |
| | | | International | N/A | Non- |
| | | | Sahab | | Respons |
| 49 | Commission | 3,000,000 | International | N/A | Non- |
| 17 | Coagulometer | | Irfan Brothers | | Respons |
| | | | International | N/A | Non- |
| | the second secon | 700,000 | Sahab | THE WAR THE WAY | Respons |
| 50 | Spectro Photometer | 700,000 | International | N/A | Non- |
| | (Semi auto chem) | | Irfan Brothers | | Respons |
| | | | International | N/A | Non- |
| | Hematology Analyzer | | Irfan Brothers | | Respons Non- |
| | | | International | N/A | Respons |
| 51 | | 2,800,000 | Sahab | | Non- |
| | | | International | N/A | Respons |
| | | SHE DOLLAR | Hoora Pharma | NIZA | Non- |
| | | | | N/A | Respons |
| 52 | Table Top Autoclave 22L | 1,800,000 | Total Technologies | 3,150,000 | |
| | | | I PCD no logica | 2,130,000 | 1st Low |

| | | | Sahab | N/A | Non- |
|---------|---------------------------------------|--|--|--------------------|----------------------------------|
| | PER PROPERTY OF STREET | Tiroso d | International Zodiac | N/A | Responsive Non- |
| -1.62 | or on organization of the second | ASSESSED OF | International Sahab | N/A | Responsive Non- |
| 53 | Laboratory Sterilizer | 4,900,000 | International Irfan Brothers International | N/A | Responsive Non- Responsive |
| | | TO NO SECTION | Total Technologies | 348,210,051 | 1st Lowest |
| 54 | CSSD | 82,500,000 | Mediland Pakistan | 393,526,720 | 2nd Lowest |
| | And the second | bayin | Total Technologies | N/A | Non- Responsive |
| 55 | Hospital Laundry | 37,500,000 | Pakistan Oxygen Ltd. | N/A | Non- Responsive |
| | a disqualification in | 37,300,000 | Mediland Pakistan | 108,812,080 | 1st Lowest |
| | feed or hadding | washing and a | Med Engineering | N/A | Non- Responsive |
| | 2018 Saloup and | the sale wit a | Pakistan Oxygen Ltd. | N/A | Non- Responsive |
| 56 | Medical Gases | 192,650,00 | Jamil Enterprise Shiga Traders | 273,768,176 N/A | 1st Lowest Non- |
| | | | Multan Chemicals | N/A | Responsive Non- |
| 57 | Biomedical Testing Equipment | up one volue a | No Bid received | N/A | Responsive N/A |
| | a complete to decrease and a | time pates que | Irfan Brothers International | N/A | Non- Responsive |
| 58 | Dental Treatment | 28,000,000 | Zodiac International | N/A | Non- Responsive |
| | | | Jamil Enterprise | 53,740,000 | 1st Lowest |
| Program | | | Executive Enterprise | N/A | Non- Responsive |
| | Bender and Second Land | Transport | Zodiac International | N/A | Non- Responsive |
| 59 | Surgical Instrument (Cardiac) | 20,000,000 | Jamil Enterprise | N/A | Non- Responsive |
| 19 40 | Cardiacy | | Executive Enterprise | N/A | Non- Responsive |
| | # # # # # # # # # # # # # # # # # # # | Ministration of the Control of the C | Itefaque Multitraders | N/A | Non- Responsive |
| 60 | Gyne Instruments | 12,500,000 | Itefaque Multitraders Zodiac | 71,046,554 | 1st Lowest |
| 1000 | 1 1100 | an season and | International | N/A | Non- Responsive |
| M | Or a | A 2 | | | 14 |
| | 1 | 1 | 0 | 1 | |

| | Jamil Enterprise | N/A | Non- |
|---------------|-------------------------|-----|----------------------------------|
| | Executive Enterprise | N/A | Responsive Non- |
| 15. FINDINGS. | Sahab International | N/A | Responsive Non- Responsive |

5. FINDINGS:

| Sr. | 15.1 SUMMARY | | | | | |
|-----|--|-----|--|--|--|--|
| No. | Particulars | - | | | | |
| i | | No, | | | | |
| ii | Total Number of Items / Packages under procurement Packages / Items against a bid to the latest and the latest | 53 | | | | |
| ii | | 49 | | | | |
| iv | Number of Packages / Items against which no bids received Number of Packages / Items against which no bids received | 04 | | | | |
| v | Evaluation Process: Number of Packages / Items against which the bidders Qualified in Technical | 30 | | | | |
| vi | Number of Packages / Items against which the bidders disqualified in Evaluation | 19 | | | | |
| | | 30 | | | | |
| ii | Number of Packages / Items against which the bidders have quoted rates within the cost of approved PC-I | 01 | | | | |
| ii | Number of Packages / Items against which the bidders have quoted rates above the cost of approved PC-I | 29 | | | | |

- The Committee found that the rates offered by the qualified firm M/s Total Technologies for the item/package No. 02 namely "BI-PAP & CPAP" is within the approved cost of PC-L
- The procurement committee found that the rates quoted by the bidders against the reaming 15.3 29 items/packages are on higher side as compared to the estimated cost of the items/packages in the approved PC-I.
- The procurement committee also found that since the PC-I was approved in year 2022 and the rates incorporated in the PC-I were based on the then prevailing market rates of bio medical equipment in the year 2020. Meanwhile, market dynamics have been changed as local currency has been devalued. Owing to significant devaluation of the Pakistani Rupee against the foreign currency and increasing inflation rates, the actual cost of the bio medical equipment has escalated beyond the approved cost for the Biomedical Equipment of the approved PC-I.

16. RECOMMNEDATIONS:

- The procurement committee recommends initiating process for the 2nd revision of the PC-I 16.1 of the PSDP project "Establishment of 50 Bedded Cardiac Hospital at Gilgit" by incorporating the rates of Biomedical Equipment received in subject bidding process.
- The procurement committee recommends that the items / packages against which no bids 16.2 have been received or against which none of the firm is responsive, a market survey shall be

conducted, and the prevailing market rates of the Bio Medical Equipment shall be incorporated in the revised PC-I of the project.

- 16.3 The packages / Items against which no firms have applied / qualified, re-bidding process shall be initiated once the revised PC-I is approved from the Competent Forum.
- 16.4 The committee recommends to award the contract to M/s Total Technologies for the supply of item/package No. 02 namely "BI-PAP & CPAP" for being responsive and quoting the rates with the approved cost of PC-I.
 - 16.5 As the rates quoted by the qualified bidders for the remaining 29 items/packages exceed the provisions of the PC-I, therefore, the committee recommends that once the latest estimated rates of Biomedical Equipment in the revised PC-1 are approved by the Competent Forum, the contracts shall be awarded only to those firms whose quoted rates are within the approved rates of the revised PC-1, subject to bid validity or any extension. Whereas the bidders whose quoted the rates above the approved rates in the revised PC-1, their financial bids / proposals may be declared as non-responsive for quoting unjustified rates.

| Sr. No. | Name Of Member | Department | Designation | Signatures |
|---------|-----------------------|--|----------------------------|------------|
| 1 | Dr Syed Sadiq Shah | EPI-Gilgit Baltistan | Director | O |
| 2 | Engr. Shahid Masood | 50 bedded Cardiac Hospital, Gilgit. | Project Director | 1 soup |
| 3 | Syed Ishtiaq Hussain | SHPI- Gilgit Baltistan | Director | |
| 4 | Dr. Faheem Iqbal | Gilgit Cardiac Hospital | Consultant Cardiologist | llg Sut |
| 5 | Aziz Haider | DD(P) | DHS Baltistan | 1 |
| 6 | Engr. Shabbir Hussain | DHS(P) Gilgit | Bio Medical Engineer | 18 |
| 7 | Muhammad Ali | FD- Gilgit Baltistan | Finance Officer | 4 |
| 8 | Muhammad Harith | P&D D GB | RO | 3 ames |
| 9 | Engr. Umair Kabeer | Punjab Institute of Cardiology, Lahore. | Bio Medical Engineer | Figures |
| 10 | Engr. Mohsin Ali | Shifa International Hospital Islamabad. | Bio Medical Engineer | 00 AVO |
| 11 | Engr. Rizwan | Rawalpindi Institute of Cardiology, Rawalpindi. | Bio Medical Engineer | Q. |
